


WARWICK LEISURE CENTRES
NEWBOLD COMYN

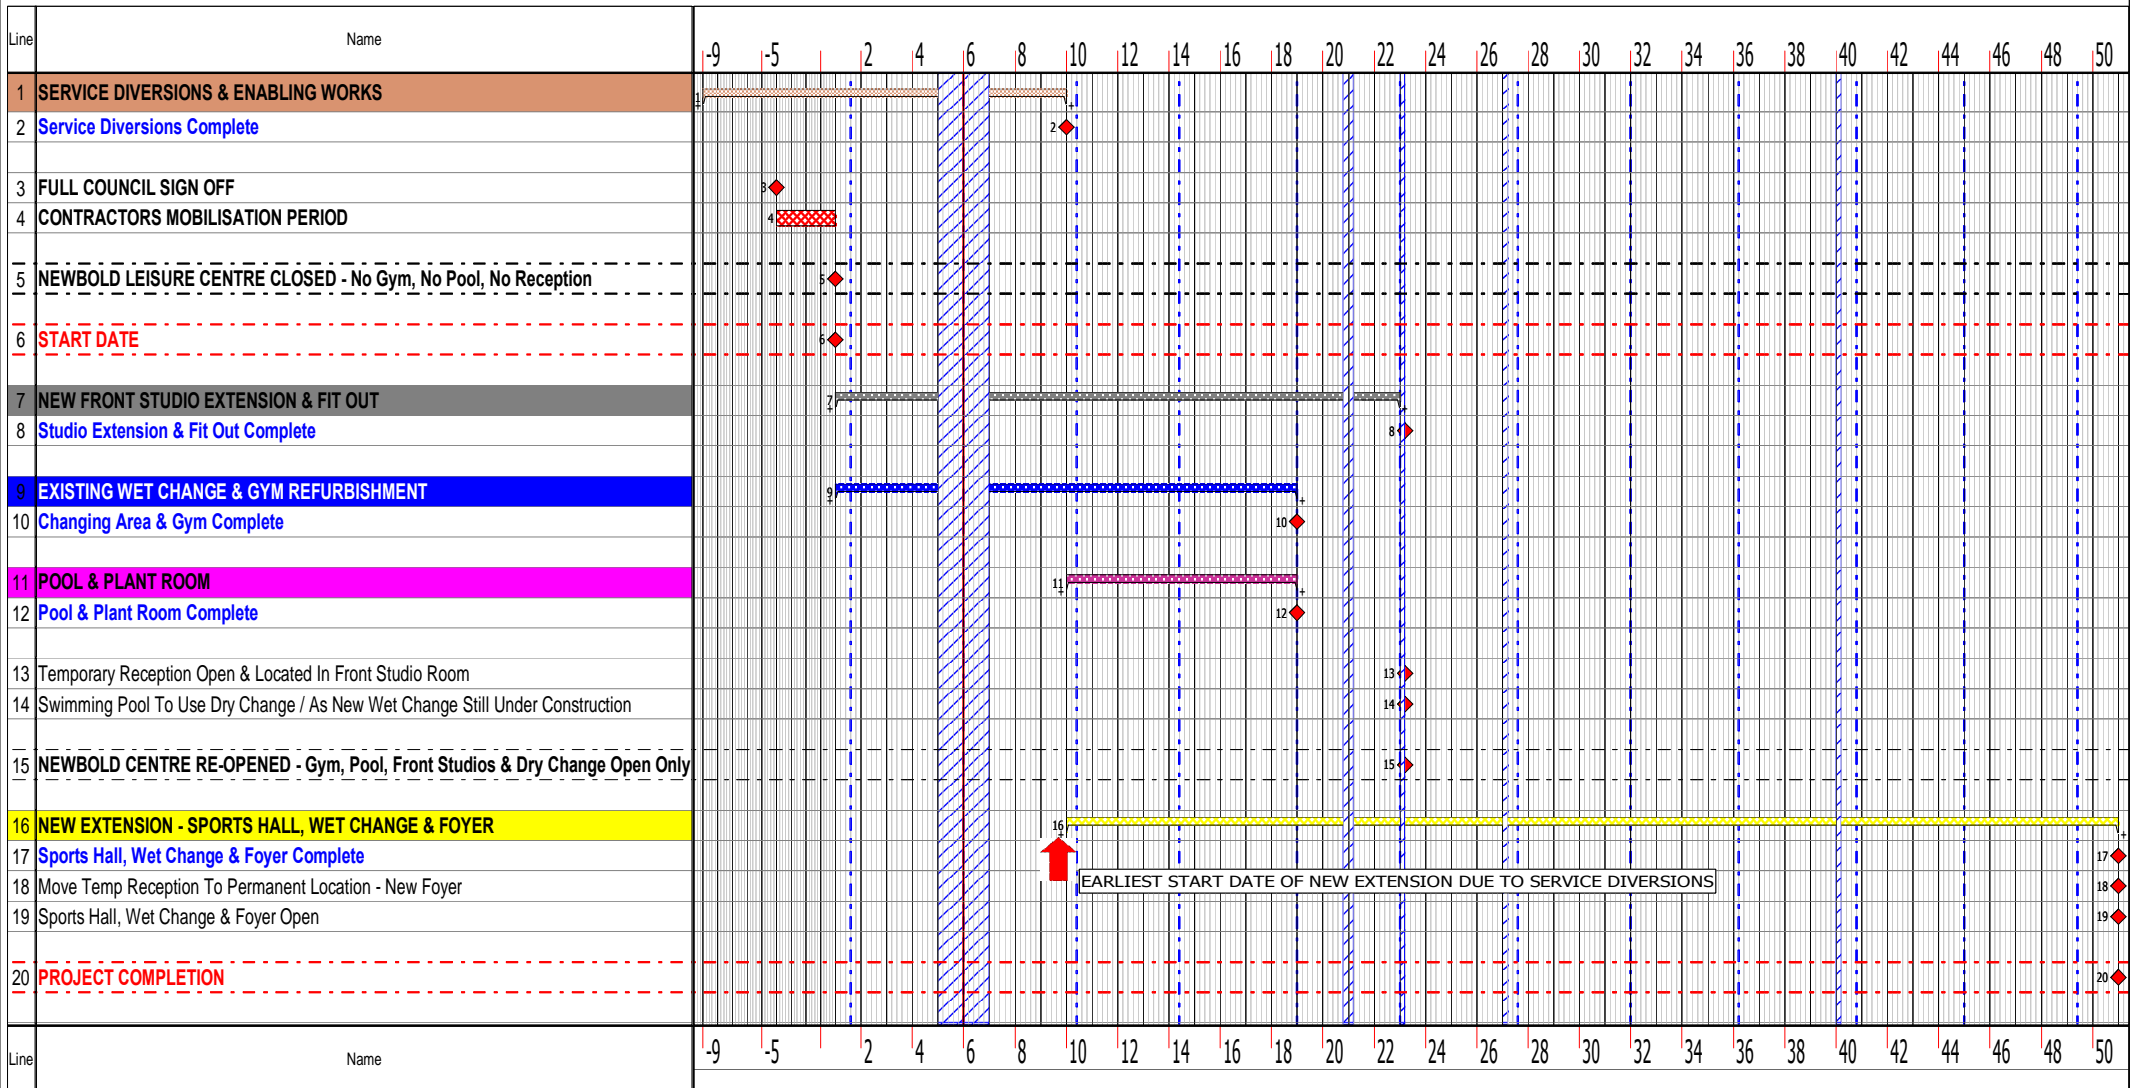

Line	Name	-9	-5	2	4	6	8	10	12	14	16	18	20	22	24	26	28	30	32	34	36	38	40	42	44	46	48	50	
1	SERVICE DIVERSIONS & ENABLING WORKS	[Bar from -9 to 10]																											
2	Service Diversions Complete	[Diamond at 10]																											
3	FULL COUNCIL SIGN OFF	[Diamond at -5]																											
4	CONTRACTORS MOBILISATION PERIOD	[Red hatched bar from -5 to 2]																											
5	NEWBOLD LEISURE CENTRE CLOSED - No Gym, No Pool, No Reception	[Dashed line from 2 to 20]																											
6	START DATE	[Red dashed line at 5]																											
7	NEW FRONT STUDIO EXTENSION & FIT OUT	[Grey hatched bar from 2 to 20]																											
8	Studio Extension & Fit Out Complete	[Diamond at 20]																											
9	EXISTING WET CHANGE & GYM REFURBISHMENT	[Blue hatched bar from 2 to 18]																											
10	Changing Area & Gym Complete	[Diamond at 18]																											
11	POOL & PLANT ROOM	[Purple hatched bar from 10 to 18]																											
12	Pool & Plant Room Complete	[Diamond at 18]																											
13	Temporary Reception Open & Located In Front Studio Room	[Diamond at 22]																											
14	Swimming Pool To Use Dry Change / As New Wet Change Still Under Construction	[Diamond at 22]																											
15	NEWBOLD CENTRE RE-OPENED - Gym, Pool, Front Studios & Dry Change Open Only	[Diamond at 22]																											
16	NEW EXTENSION - SPORTS HALL, WET CHANGE & FOYER	[Yellow hatched bar from 10 to 50]																											
17	Sports Hall, Wet Change & Foyer Complete	[Diamond at 50]																											
18	Move Temp Reception To Permanent Location - New Foyer	[Diamond at 50]																											
19	Sports Hall, Wet Change & Foyer Open	[Diamond at 50]																											
20	PROJECT COMPLETION	[Red dashed line at 50]																											

Revision: Revision Date: 26/09/2016
Comment: A

Prog No T2823-SP01	Drawn By AD	Drawn Date 26/09/2016	Program Status Tender Stage
-----------------------	----------------	--------------------------	---------------------------------------
